

Kentucky Utilities Company and Louisville Gas and Electric Company
AMI Quarterly Implementation and Deployment Status Report
Case Nos. 2020-00349 & 2020-00350
July 31, 2025

Executive Summary:

In accordance with the Kentucky Public Service Commission's Order of June 30, 2021, and subsequent order of December 6, 2021, in Case Nos. 2020-00349 and 2020-00350, Kentucky Utilities Company and Louisville Gas and Electric Company ("Companies") submit the sixteenth quarterly progress report on the 2021 AMI plan. The quarterly report provides a status of the implementation and deployment of the project, adherence to budgets, adherence to timeliness, any significant change orders, number of AMI meters implemented, and the number of non-AMI meters removed and retired. This report covers the period from the June 30, 2021, order through June 30, 2025, except where otherwise noted.

The project is performing consistent with planned expenditures and the overall timeline is on schedule, with full deployment still expected to be complete by December 31, 2025.

Financial

The project is performing consistent with planned expenditures.

Project Spend (\$000)			
	Project to Date Spend	Forecasted Total Project	Remaining Project Amount
CWIP	\$320,380	\$352,068	\$31,688
AMI Implementation Expenses	\$35,917	\$39,802 ¹	\$3,885

Schedule

Major activities:

- Installed over 1,339,000 AMI meters and modules.
- AMI network deployments are active in KU's and LG&E's service territories.
 - 217 of 222 gateways installed (98% complete)
 - 2,888 of 2,906 routers installed (99% complete)
- 4,213 customer account opt-outs. The 4,213 is approximately 0.32% of customers who have had the opportunity to opt out vs 0.80% that was estimated in the plan.
- Installed 16,950 Gas Encoder Receiver Transmitters (ERT) in our gas only territory.

Upcoming major activities:

- AMI meter deployment will continue through 2025.
- Build-out of the AMI network gateway and router installations will continue through 2025.
- Release 4 (Customer Engagement Tools) reflects current plan with tools and enhancements going live throughout 2025.
- Release 5 (Distribution Integration) on schedule to accomplish Conservation Voltage Reduction (CVR) and outage management improvements in 2025.

¹ The \$39,802 includes \$3M of expense currently included in base rates.


Kentucky Utilities Company and Louisville Gas and Electric Company

AMI Quarterly Implementation and Deployment Status Report

Case Nos. 2020-00349 & 2020-00350

July 31, 2025

Project schedule:

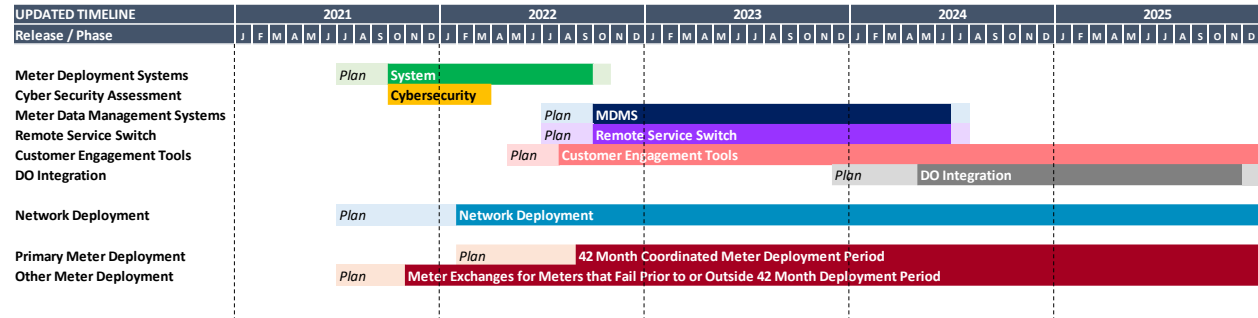

Significant Contract Change Orders

No significant change orders to report.

Meter Deployment

Company	Number of AMI Meters/Modules Installed ²	Number of AMI Meters/Modules ⁴ Installed since 9/22	Number of Non-AMI Meters retired ³
LG&E- Electric	443,740	443,104	413,095
LG&E – Gas	311,660	311,660	
KU	584,419	584,313	555,377
Total	1,339,819	1,339,077	968,472

² These include AMI meters installed for the Solar Share Program, DSM AMS Opt-In Program, and downtown network since program inception.

³ Electric meters removed for retirement in July 2021 through June 2025 in the meter asset management system.

⁴ Modules are installed on gas meters to enable remote meter reading AMI capabilities.
