

E.W. Brown BESS Project Schedule

ID	Task Name	Duration	Start	Finish	Predecessors	2022				2023				2024				2025				2026				2027							
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4				
1	E.W Brown BESS Project	2036 days	Mon 04/18/22	Sat 11/13/27		[Gantt bar spanning from 04/18/22 to 11/13/27]																											
2																																	
3	Project Development	185 days	Mon 04/18/22	Thu 10/20/22		[Gantt bar from 04/18/22 to 10/20/22]																											
4	Feasibility Study	95 days	Mon 04/18/22	Fri 07/22/22		[Gantt bar from 04/18/22 to 07/22/22]																											
5	Contract Award	0 days	Tue 04/26/22	Tue 04/26/22		[Milestone diamond at 04/26/22]																											
6	Kickoff Meeting	0 days	Mon 04/18/22	Mon 04/18/22		[Milestone diamond at 04/18/22]																											
7	Project Site Rankings	0 days	Fri 05/20/22	Fri 05/20/22		[Milestone diamond at 05/20/22]																											
8	Site Layouts and Generation Potential	0 days	Fri 06/10/22	Fri 06/10/22		[Milestone diamond at 06/10/22]																											
9	Listing of Potential Offsite Locations	0 days	Fri 06/17/22	Fri 06/17/22		[Milestone diamond at 06/17/22]																											
10	Draft Feasibility Report	0 days	Fri 07/01/22	Fri 07/01/22		[Milestone diamond at 07/01/22]																											
11	Final Feasibility Report	0 days	Fri 07/22/22	Fri 07/22/22		[Milestone diamond at 07/22/22]																											
12	Conceptual Design	60 days	Sun 08/21/22	Thu 10/20/22		[Gantt bar from 08/21/22 to 10/20/22]																											
13	Contract Award	0 days	Sun 08/21/22	Sun 08/21/22	11FS+30 days	[Milestone diamond at 08/21/22]																											
14	Site Layout & Improvements	60 days	Sun 08/21/22	Wed 10/19/22	13	[Gantt bar from 08/21/22 to 10/19/22]																											
15	Specifications	60 days	Sun 08/21/22	Wed 10/19/22	13	[Gantt bar from 08/21/22 to 10/19/22]																											
16	CPCN Support Data	30 days	Sun 08/21/22	Mon 09/19/22	13	[Gantt bar from 08/21/22 to 09/19/22]																											
17	Interconnection Support Data	30 days	Sun 08/21/22	Mon 09/19/22	13	[Gantt bar from 08/21/22 to 09/19/22]																											
18	Issue Bid Documents	0 days	Thu 10/20/22	Thu 10/20/22	14,15	[Milestone diamond at 10/20/22]																											
19																																	
20	Generation RFP	122 days	Wed 06/15/22	Sat 10/15/22		[Gantt bar from 06/15/22 to 10/15/22]																											
21	Issue RFP	0 days	Wed 06/15/22	Wed 06/15/22		[Milestone diamond at 06/15/22]																											
22	Bid Period	61 days	Wed 06/15/22	Sun 08/14/22	21	[Gantt bar from 06/15/22 to 08/14/22]																											
23	Bid Responses Due	0 days	Mon 08/15/22	Mon 08/15/22	22	[Milestone diamond at 08/15/22]																											
24	RFP Analysis	61 days	Mon 08/15/22	Fri 10/14/22	23	[Gantt bar from 08/15/22 to 10/14/22]																											
25	RFP Analysis Completed	0 days	Sat 10/15/22	Sat 10/15/22	24	[Milestone diamond at 10/15/22]																											
26																																	
27	IC Partial Project Sanction	50 days	Sat 10/15/22	Sat 12/03/22	25,11	[Gantt bar from 10/15/22 to 12/03/22]																											
28																																	
29	Interconnection	910 days	Fri 06/03/22	Fri 11/29/24		[Gantt bar from 06/03/22 to 11/29/24]																											
30	File LGIR	0 days	Fri 06/03/22	Fri 06/03/22		[Milestone diamond at 06/03/22]																											
31	Queue	365 days	Fri 06/03/22	Fri 06/02/23	30	[Gantt bar from 06/03/22 to 06/02/23]																											
32	Electrical Interconnection Studies	365 days	Sat 06/03/23	Sat 06/01/24	31	[Gantt bar from 06/03/23 to 06/01/24]																											
33	Execute LGIA	0 days	Sun 06/02/24	Sun 06/02/24	32	[Milestone diamond at 06/02/24]																											

Project: E.W. Brown BESS Project Date: Tue 08/02/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

E.W. Brown NGCC Project Schedule

ID	Task Name	Duration	Start	Finish	2022		2023				2024				2025				2026				2027				2028					
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2		
1	E.W. Brown NGCC	2187 days	Mon 04/04/22	Wed 03/29/28	[Gantt bar spanning from Q1 2022 to Q2 2028]																											
2																																
3	Project Development	827 days	Mon 04/04/22	Mon 07/08/24	[Gantt bar spanning from Q1 2022 to Q3 2024]																											
4	Concept Development	121 days	Mon 04/04/22	Tue 08/02/22	[Task bar from Q1 2022 to Q2 2022]																											
5	Bid Submittal Approval	14 days	Wed 08/03/22	Tue 08/16/22	[Task bar in Q2 2022]																											
6	Management Approval to Proceed with Development	2 days	Sun 10/02/22	Mon 10/03/22	[Task bar in Q3 2022]																											
7	IC Approval of EPC Agreement	35 days	Tue 06/04/24	Mon 07/08/24	[Task bar in Q3 2024]																											
8																																
9	E.W. Brown Demo	861 days	Wed 10/05/22	Tue 02/11/25	[Gantt bar spanning from Q4 2022 to Q1 2025]																											
10	Award BR 1-2 or Demo Award	60 days	Wed 10/05/22	Sat 12/03/22	[Task bar in Q4 2022]																											
11	Demo Activities	769 days	Tue 01/03/23	Sun 02/09/25	[Task bar spanning from Q1 2023 to Q4 2024]																											
12	BR Demo Complete	1 day	Tue 02/11/25	Tue 02/11/25	[Task bar in Q1 2025]																											
13																																
14	Generation RFP	102 days	Wed 06/22/22	Sat 10/01/22	[Gantt bar spanning from Q2 2022 to Q3 2022]																											
15	Issue RFP	1 day	Wed 06/22/22	Wed 06/22/22	[Task bar in Q2 2022]																											
16	Bid Period	56 days	Thu 06/23/22	Wed 08/17/22	[Task bar in Q2 2022]																											
17	Bid Responses Due	0 days	Thu 08/18/22	Thu 08/18/22	[Task bar in Q3 2022]																											
18	RFP Analysis	44 days	Thu 08/18/22	Fri 09/30/22	[Task bar in Q3 2022]																											
19	RFP Analysis Completed	1 day	Sat 10/01/22	Sat 10/01/22	[Task bar in Q4 2022]																											
20																																
21	Interconnection	1902 days	Tue 06/21/22	Sat 09/04/27	[Gantt bar spanning from Q2 2022 to Q4 2027]																											
22	File LGIR	1 day	Tue 06/21/22	Tue 06/21/22	[Task bar in Q2 2022]																											
23	Electrical Interconnection Studies	733 days	Thu 06/23/22	Mon 06/24/24	[Task bar spanning from Q2 2022 to Q4 2024]																											
24	Execute LGIA	1 day	Wed 06/26/24	Wed 06/26/24	[Task bar in Q4 2024]																											
25	Electrical Interconnection Upgrades	730 days	Wed 09/03/25	Thu 09/02/27	[Task bar spanning from Q3 2025 to Q4 2027]																											
26	Electrical Interconnection Complete	1 day	Sat 09/04/27	Sat 09/04/27	[Task bar in Q4 2027]																											
27																																
28	Permitting	728 days	Sun 07/03/22	Sat 06/29/24	[Gantt bar spanning from Q3 2022 to Q4 2024]																											
29	Air Permit	728 days	Sun 07/03/22	Sat 06/29/24	[Gantt bar spanning from Q3 2022 to Q4 2024]																											
30	Air Permit Netting Analysis	31 days	Sun 07/03/22	Tue 08/02/22	[Task bar in Q3 2022]																											
31	Application Preparation	117 days	Wed 02/01/23	Sun 05/28/23	[Task bar in Q1 2023]																											
32	File Air Permit Application	1 day	Mon 05/29/23	Mon 05/29/23	[Task bar in Q2 2023]																											
33	Air Permit Review	365 days	Wed 05/31/23	Wed 05/29/24	[Task bar spanning from Q3 2023 to Q4 2024]																											
34	Receive Final Air Permit	31 days	Thu 05/30/24	Sat 06/29/24	[Task bar in Q4 2024]																											
35																																

Project: Brown Schedule 8-5-20 Date: Mon 08/15/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

Mercer County Solar Project Schedule

ID	Task Name	Duration	Start	Finish	Predecessors	2022				2023				2024				2025				2026				2027							
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4				
1	Mercer County Solar Project	1966 days	Mon 04/18/22	Sat 09/04/27		[Gantt bar spanning from 04/18/22 to 09/04/27]																											
2																																	
3	Project Development	185 days	Mon 04/18/22	Thu 10/20/22		[Gantt bar spanning from 04/18/22 to 10/20/22]																											
4	Feasibility Study	95 days	Mon 04/18/22	Fri 07/22/22		[Gantt bar spanning from 04/18/22 to 07/22/22]																											
5	Contract Award	0 days	Tue 04/26/22	Tue 04/26/22		[Milestone diamond at 04/26/22]																											
6	Kickoff Meeting	0 days	Mon 04/18/22	Mon 04/18/22		[Milestone diamond at 04/18/22]																											
7	Project Site Rankings	0 days	Fri 05/20/22	Fri 05/20/22		[Milestone diamond at 05/20/22]																											
8	Site Layouts and Generation Potential	0 days	Fri 06/10/22	Fri 06/10/22		[Milestone diamond at 06/10/22]																											
9	Listing of Potential Offsite Locations	0 days	Fri 06/17/22	Fri 06/17/22		[Milestone diamond at 06/17/22]																											
10	Draft Feasibility Report	0 days	Fri 07/01/22	Fri 07/01/22		[Milestone diamond at 07/01/22]																											
11	Final Feasibility Report	0 days	Fri 07/22/22	Fri 07/22/22		[Milestone diamond at 07/22/22]																											
12	Conceptual Design	60 days	Sun 08/21/22	Thu 10/20/22		[Gantt bar spanning from 08/21/22 to 10/20/22]																											
13	Contract Award	0 days	Sun 08/21/22	Sun 08/21/22	11FS+30 days	[Milestone diamond at 08/21/22]																											
14	Site Layout & Improvements	60 days	Sun 08/21/22	Wed 10/19/22	13	[Gantt bar spanning from 08/21/22 to 10/19/22]																											
15	Specifications	60 days	Sun 08/21/22	Wed 10/19/22	13	[Gantt bar spanning from 08/21/22 to 10/19/22]																											
16	CPCN Support Data	30 days	Sun 08/21/22	Mon 09/19/22	13	[Gantt bar spanning from 08/21/22 to 09/19/22]																											
17	Interconnection Support Data	30 days	Sun 08/21/22	Mon 09/19/22	13	[Gantt bar spanning from 08/21/22 to 09/19/22]																											
18	Issue Bid Documents	0 days	Thu 10/20/22	Thu 10/20/22	14,15	[Milestone diamond at 10/20/22]																											
19																																	
20	Generation RFP	122 days	Wed 06/15/22	Sat 10/15/22		[Gantt bar spanning from 06/15/22 to 10/15/22]																											
21	Issue RFP	0 days	Wed 06/15/22	Wed 06/15/22		[Milestone diamond at 06/15/22]																											
22	Bid Period	61 days	Wed 06/15/22	Sun 08/14/22	21	[Gantt bar spanning from 06/15/22 to 08/14/22]																											
23	Bid Responses Due	0 days	Mon 08/15/22	Mon 08/15/22	22	[Milestone diamond at 08/15/22]																											
24	RFP Analysis	61 days	Mon 08/15/22	Fri 10/14/22	23	[Gantt bar spanning from 08/15/22 to 10/14/22]																											
25	RFP Analysis Completed	0 days	Sat 10/15/22	Sat 10/15/22	24	[Milestone diamond at 10/15/22]																											
26																																	
27	IC Partial Project Sanction	50 days	Sat 10/15/22	Sat 12/03/22	25,11	[Gantt bar spanning from 10/15/22 to 12/03/22]																											
28																																	
29	Interconnection	910 days	Fri 06/03/22	Fri 11/29/24		[Gantt bar spanning from 06/03/22 to 11/29/24]																											
30	File LGIR	0 days	Fri 06/03/22	Fri 06/03/22		[Milestone diamond at 06/03/22]																											
31	Queue	365 days	Fri 06/03/22	Fri 06/02/23	30	[Gantt bar spanning from 06/03/22 to 06/02/23]																											
32	Electrical Interconnection Studies	365 days	Sat 06/03/23	Sat 06/01/24	31	[Gantt bar spanning from 06/03/23 to 06/01/24]																											
33	Execute LGIA	0 days	Sun 06/02/24	Sun 06/02/24	32	[Milestone diamond at 06/02/24]																											
34	Electrical Interconnection Upgrades	180 days	Sun 06/02/24	Thu 11/28/24	33	[Gantt bar spanning from 06/02/24 to 11/28/24]																											
35	Electrical Interconnection Complete	0 days	Fri 11/29/24	Fri 11/29/24	34	[Milestone diamond at 11/29/24]																											
36																																	


Project: Mercer County Solar Pr	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

Mill Creek NGCC Project Schedule

ID	Task Name	Duration	Start	Finish	2022		2023				2024				2025				2026					
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2		
1	Mill Creek NGCC	1822 days	Mon 04/04/22	Tue 03/30/27	[Gantt Chart showing project summary bar from Q1 2022 to Q2 2026]																			
2																								
3	Project Development	679 days	Mon 04/04/22	Sun 02/11/24	[Gantt Chart showing project summary bar from Q1 2022 to Q4 2023]																			
4	Concept Development	121 days	Mon 04/04/22	Tue 08/02/22	[Gantt Chart showing task bar from Q1 2022 to Q2 2022]																			
5	Development Plan Approval	14 days	Wed 08/03/22	Tue 08/16/22	[Gantt Chart showing task bar from Q2 2022 to Q3 2022]																			
6	Management Approval to Proceed with Development	2 days	Sun 10/02/22	Mon 10/03/22	[Gantt Chart showing task bar from Q3 2022 to Q3 2022]																			
7	IC Approval of EPC Agreement	31 days	Fri 01/12/24	Sun 02/11/24	[Gantt Chart showing task bar from Q4 2023 to Q1 2024]																			
8																								
9	Generation RFP	102 days	Wed 06/22/22	Sat 10/01/22	[Gantt Chart showing project summary bar from Q2 2022 to Q4 2022]																			
10	Issue RFP	1 day	Wed 06/22/22	Wed 06/22/22	[Gantt Chart showing task bar at start of Q2 2022]																			
11	Bid Period	55 days	Thu 06/23/22	Tue 08/16/22	[Gantt Chart showing task bar from Q2 2022 to Q3 2022]																			
12	Bid Responses Due	1 day	Wed 08/17/22	Wed 08/17/22	[Gantt Chart showing task bar at end of Q2 2022]																			
13	RFP Analysis	44 days	Thu 08/18/22	Fri 09/30/22	[Gantt Chart showing task bar from Q3 2022 to Q3 2022]																			
14	RFP Analysis Completed	1 day	Sat 10/01/22	Sat 10/01/22	[Gantt Chart showing task bar at end of Q3 2022]																			
15																								
16	Interconnection	1564 days	Tue 06/21/22	Thu 10/01/26	[Gantt Chart showing project summary bar from Q2 2022 to Q4 2025]																			
17	File LGIR	1 day	Tue 06/21/22	Tue 06/21/22	[Gantt Chart showing task bar at start of Q2 2022]																			
18	Electrical Interconnection Studies	733 days	Thu 06/23/22	Mon 06/24/24	[Gantt Chart showing task bar from Q2 2022 to Q4 2023]																			
19	Execute LGIA	1 day	Wed 06/26/24	Wed 06/26/24	[Gantt Chart showing task bar at end of Q4 2023]																			
20	Electrical Interconnection Upgrades	555 days	Tue 03/25/25	Wed 09/30/26	[Gantt Chart showing task bar from Q1 2024 to Q4 2025]																			
21	Electrical Interconnection Complete	1 day	Thu 10/01/26	Thu 10/01/26	[Gantt Chart showing task bar at end of Q4 2025]																			
22																								
23	Permitting	584 days	Sun 07/03/22	Tue 02/06/24	[Gantt Chart showing project summary bar from Q3 2022 to Q2 2024]																			
24	Air Permit	584 days	Sun 07/03/22	Tue 02/06/24	[Gantt Chart showing project summary bar from Q3 2022 to Q2 2024]																			
25	Air Permit Netting Analysis	31 days	Sun 07/03/22	Tue 08/02/22	[Gantt Chart showing task bar from Q3 2022 to Q3 2022]																			
26	Application Preparation	87 days	Wed 10/05/22	Fri 12/30/22	[Gantt Chart showing task bar from Q3 2022 to Q4 2022]																			
27	File Air Permit Application	1 day	Sat 12/31/22	Sat 12/31/22	[Gantt Chart showing task bar at end of Q4 2022]																			
28	Air Permit Review	371 days	Sun 01/01/23	Sat 01/06/24	[Gantt Chart showing task bar from Q1 2023 to Q2 2024]																			
29	Receive Final Air Permit	31 days	Sun 01/07/24	Tue 02/06/24	[Gantt Chart showing task bar from Q2 2024 to Q2 2024]																			
30																								
31	CPCN Site Compatibility	490 days	Wed 10/05/22	Tue 02/06/24	[Gantt Chart showing project summary bar from Q4 2022 to Q2 2024]																			
32	CPCN Site Compatibility Application Preparation	87 days	Wed 10/05/22	Fri 12/30/22	[Gantt Chart showing task bar from Q4 2022 to Q1 2023]																			
33	File CPCN Site Compatibility Application	1 day	Sat 12/31/22	Sat 12/31/22	[Gantt Chart showing task bar at end of Q4 2022]																			
34	CPCN Site Compatibility Review	371 days	Sun 01/01/23	Sat 01/06/24	[Gantt Chart showing task bar from Q1 2023 to Q2 2024]																			
35	Receive CPCN Site Compatibility Order	31 days	Sun 01/07/24	Tue 02/06/24	[Gantt Chart showing task bar from Q2 2024 to Q2 2024]																			

Project: Mill Creek Schedule 8-5 Date: Mon 08/15/22	Task	[Blue Bar] Project Summary	[Grey Bar] Manual Task	[Light Blue Bar] Start-only	[Dark Blue Bar] Finish-only	[Red Line] Deadline	[Green Arrow] Progress
	Split	[Dotted Line] Inactive Task	[White Bar] Duration-only	[Light Blue Bar] External Tasks	[Dark Blue Bar] External Milestone	[Grey Bar] Manual Progress	[Blue Line] Progress
	Milestone	[Diamond] Inactive Milestone	[Diamond] Manual Summary Rollup	[Dark Blue Bar] External Milestone	[Diamond] External Milestone	[Grey Bar] Manual Progress	[Blue Line] Progress
	Summary	[Thick Blue Bar] Inactive Summary	[Thick Grey Bar] Manual Summary	[Thick Blue Bar] External Milestone	[Diamond] External Milestone	[Grey Bar] Manual Progress	[Blue Line] Progress

Mill Creek NGCC Project Schedule

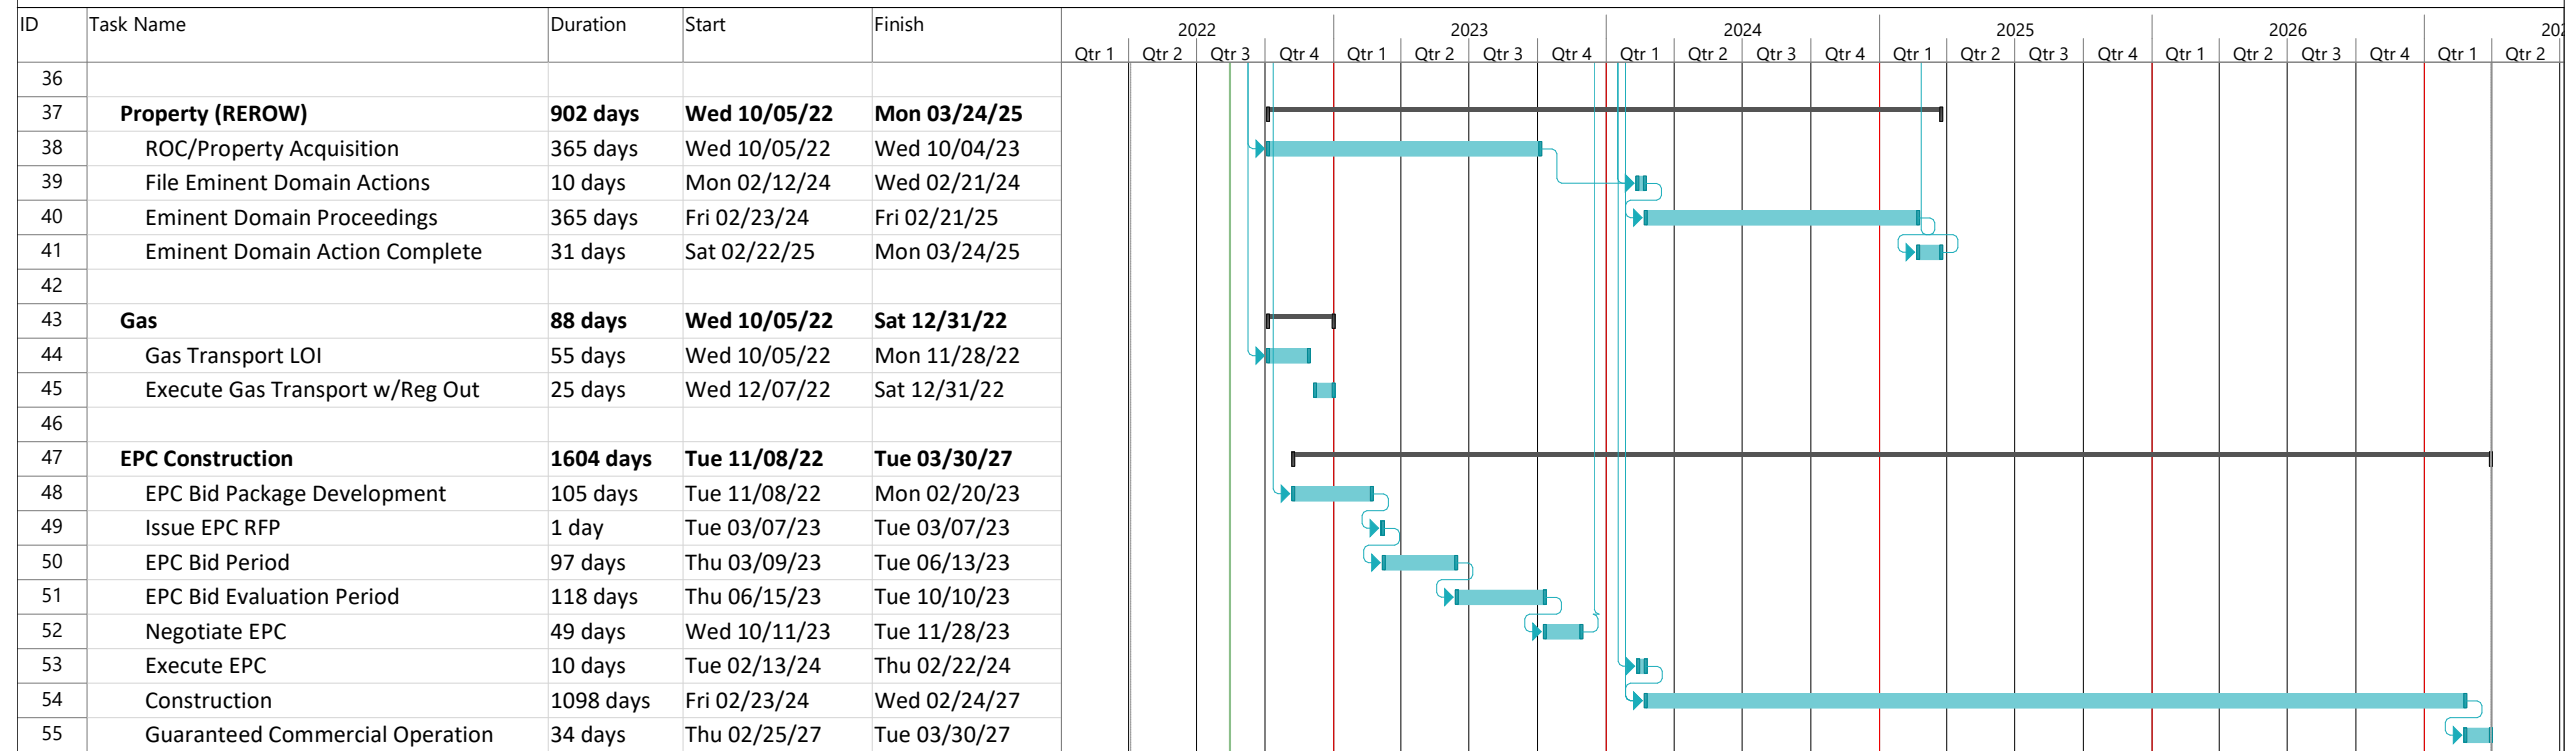

Project: Mill Creek Schedule 8-5 Date: Mon 08/15/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
